

PRECONSTRUCTION MEETING

Date: 2/11/15

Contractor: C.J. Moyna & Sons, Inc.

Project No(s): 91-0352-051

PCC Pavement - Grade/Replace, Lighting, Traffic Signs

Name	Representing	Phone#	Call #	E-mail
Scott Sommers, P.E.	IA D.O.T.-Chariton RCE	641-774-5056	515-450-6879	scott.sommers@dot.iowa.gov
Kyle Hardin, Const. Tech. Supervisor	IA D.O.T.-Chariton RCE	641-774-5056	641-774-6741	kyle.hardin@dot.iowa.gov
Liz Finarty, P.E.	IA D.O.T.-Chariton RCE	641-774-5056	641-777-2871	liz.finarty@dot.iowa.gov
Mike Kaller, Project Inspector	IA D.O.T.-Chariton RCE	641-774-5056	641-777-5285	william.kaller@dot.iowa.gov
Tammy JENSEN	IA DOT		641-777-4652	tammy.jensen@dot.iowa.gov
DAVID CARROLL	WARREN COUNTY (SIS) 961-1050	(SIS) 767-0333		david@co.warren.ia.us
Corr T. Buhl	Warren County (SIS) 961-1050	(SIS) 999-8753		Corb @ Co. Warren, IA, US
CHARL BARNER	CITY OF INDIANOLA	515-313-8682		CBARNER@CITYOFINDIANOLA.GOV
AR Powers	PIE ENGINEERING Co.	515-999-3083		ARPOWERS@PIENGR.COM
Bob Miller	Indianola Municipal	515-802-1181		bmillerdj-m-l.com
Loa Elbert	Indianola Water	515-249-6986		elbert@I-A-U-COM
Dale Schwab	Cedar Falls Const 319-235-6796	319-404-5162		dale@cedarfallsconstruction.com
Tom Bowler	Cedar Valley Corp	319-290-5611		tbowler@cedarvalleycorp.com
Pat Young	C.J. Moyna & Sons	563-880-7072		pyoung@cjmoyna.com
Ryan King	CJ Moyna & Sons	563-980-7688		rking@cjmoyna.com
Travis Augustyn	Progressive Smart Wires	563-880-9138		taugustyn@progressivesmartwires.com
Scott Dillard	The Driller, LLC	515-210-5152		scottdillard@thedrillerllc.com
GENE BRAUN	DES MOINES ASPHALT	515-240-6129		gbraun@dmamidwest.com
Bob Leader	Leader Construction	515-988-8988		Leaderconstruction@gmail.com
Mrs. Winkler	Leader Construction	515-988-7001		
Bryson Winksky	Barth & West (Warren Natel)	605-680-9368		bryson.winksky@barthwest.com
Stans Ripberger	Warren Water District	575-248-5352		SRipberger@WarrenWaterDistrict.com
Randy Bearers	Warren Water District	515-240-6227		rbearers@WarrenWaterDistrict.com
Date 07/3/15	IA DOT	641-774-2900		dale.obrien@dot.iowa.gov

PRECONSTRUCTION MEETING


Date: 2/11/15

Contractor: C.J. Moyna & Sons, Inc.

Project No(s): 91-0352-051

PCC Pavement - Grade/Replace, Lighting, Traffic Signs

Name	Representing	Phone#	Cell #	E-mail
Scott Sommers, P.E.	IA D.O.T.-Chariton RCE	641-774-5056	515-450-6879	scott.sommers@dot.iowa.gov
Kyle Hardin, Const. Tech. Supervisor	IA D.O.T.-Chariton RCE	641-774-5056	641-774-6741	kyle.hardin@dot.iowa.gov
Liz Finarty, P.E.	IA D.O.T.-Chariton RCE	641-774-5056	641-777-2871	liz.finarty@dot.iowa.gov
Mike Kaller, Project Inspector	IA D.O.T.-Chariton RCE	641-774-5056	641-777-5285	william.kaller@dot.iowa.gov
Bryan Bradley	IA DOT Traffic Safety	515 239 1014		bryan.bradley@iowa.gov
Jacob Hour	DOT - Des Moines	515-239-1916		jasen.h@dot.iowa.gov
JOSH DOUGHAN	McCURRE ENGINEERS	515.505.4106		jdoughan@mcresults.com
DEREK AULEMAN	"	480.353.9800		dalleman@mcresults.com
Ed Miner	Contractors of IA	515 303 3763		ed.miner@contractorsia.com ed.miner@contractorsia.com
Bob Brunig	Pond E Engineering	515-393-8773		RwBrunig@PEENG.com
Todd Metcalf	IA DOT Marketplace	515-250-3374		todd.metcalf@dot.iowa.gov
Jeff Vroom	JMT Trucking	515-333-0660		jvroom@citruking.com
Brian Seymour	City of Indiana Fire/EMS	515-371-3222		bseymour@cityofindiana.com
Mike Metcalf	Indianola Municipal Utilities	515-975-5447		mmetcalf@i-m-u.com
Todd Kielkopf	"	515-681-1297		toddkielkopf@i-m-u.com
Ed Chick	CENTURYLINK	515-290-2035		Ed.Chick@CENTURYLINK.COM
KENN HOFFMAN	CENTURYLINK	515-943-3336		KENN.HOFFMAN@CENTURYLINK.COM
BRAD FREEMAN	STERNQUIST	515-975-3642		bfreeman@sternquistconstruction.com

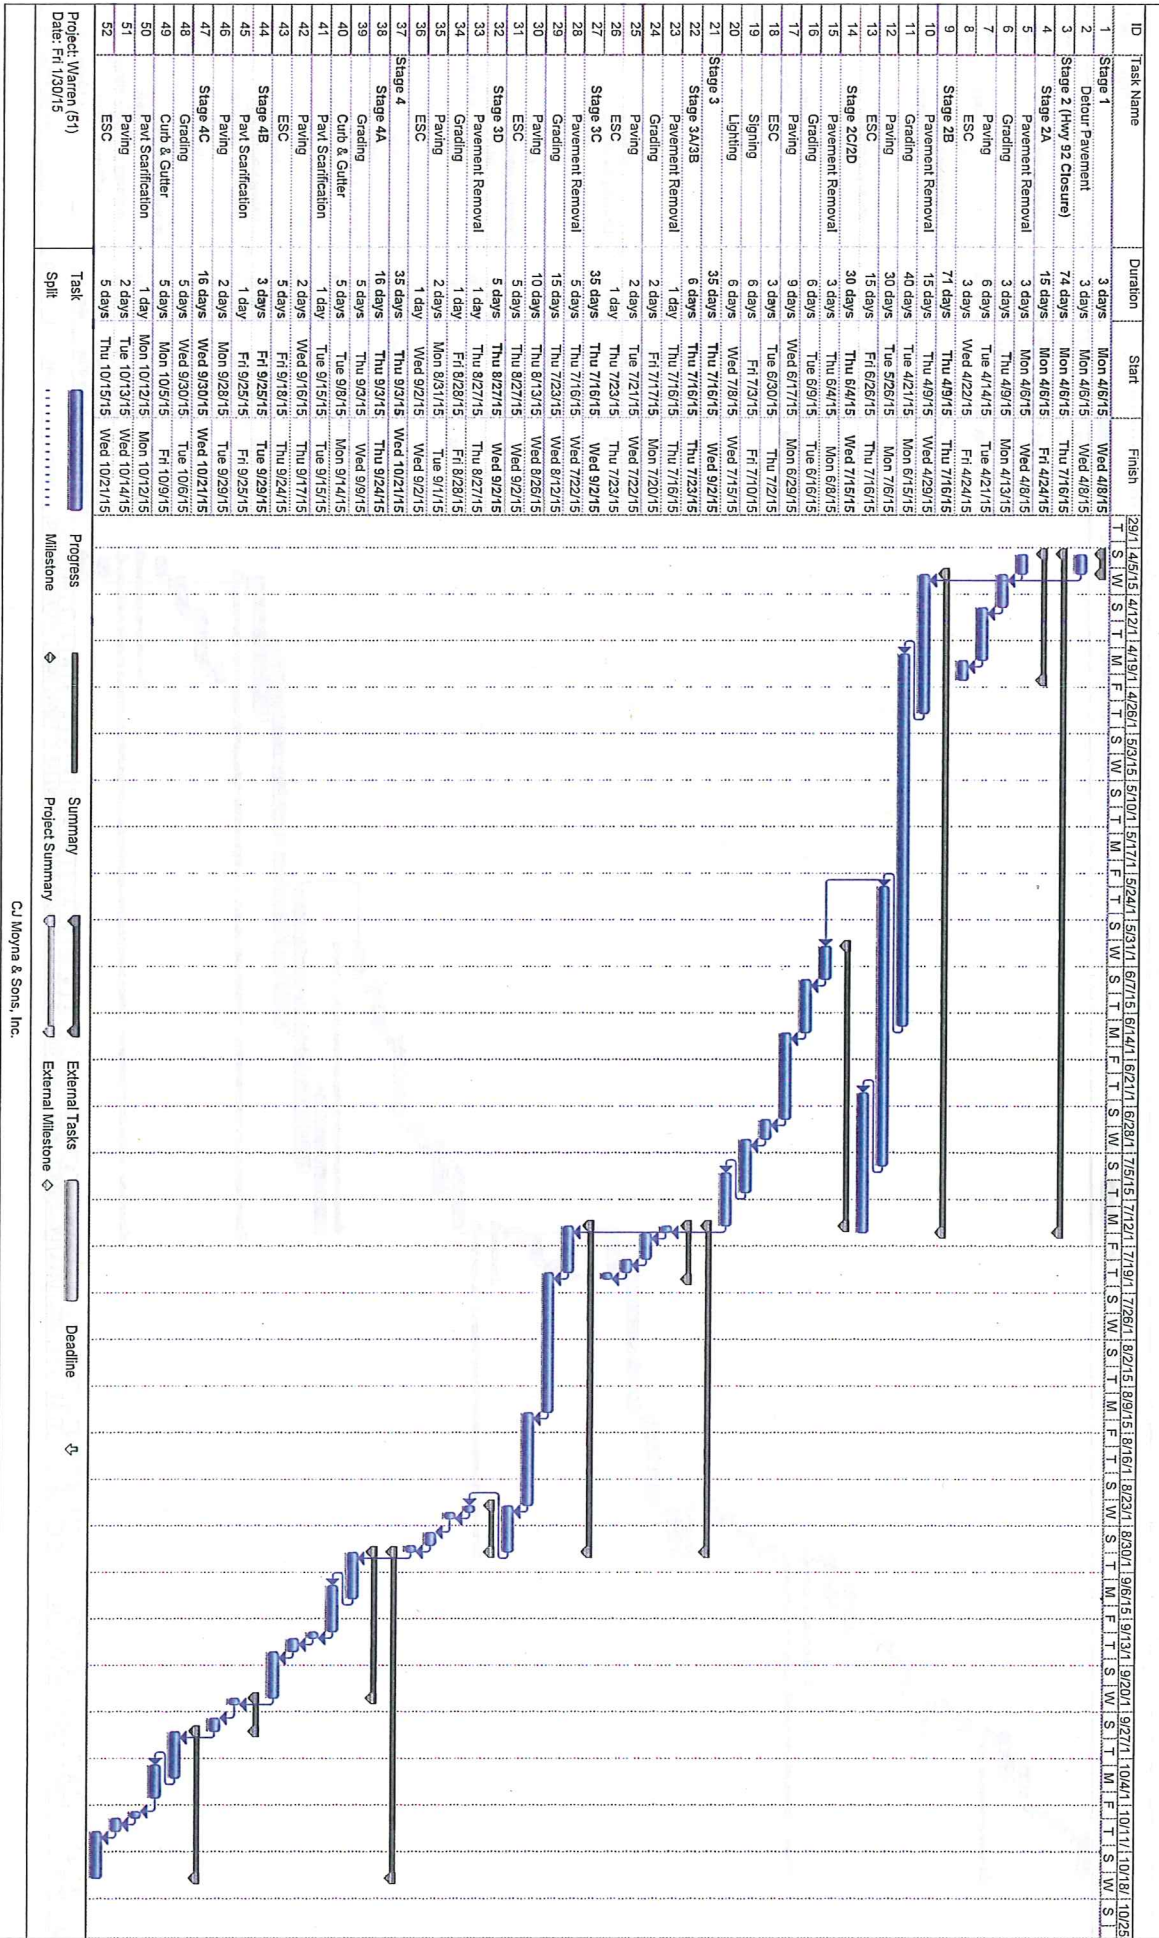

ID	Task Name	Duration	Start	Finish	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025
1	Stage 1	3 days	Mon 4/6/15	Wed 4/8/15															
2	Debour Pavement	3 days	Mon 4/6/15	Wed 4/8/15															
3	Stage 2 (Hwy 92 Closure)	74 days	Mon 4/6/15	Thu 7/16/15															
4	Stage 2A	15 days	Mon 4/6/15	Fri 4/24/15															
5	Pavement Removal	3 days	Mon 4/6/15	Wed 4/8/15															
6	Grading	3 days	Thu 4/9/15	Mon 4/13/15															
7	Paving	6 days	Thu 4/14/15	Tue 4/21/15															
8	ESC	3 days	Wed 4/22/15	Fri 4/24/15															
9	Stage 2B	71 days	Thu 4/9/15	Thu 7/16/15															
10	Pavement Removal	15 days	Thu 4/9/15	Wed 4/29/15															
11	Grading	40 days	Tue 4/21/15	Mon 6/15/15															
12	Paving	30 days	Tue 5/26/15	Mon 7/6/15															
13	ESC	15 days	Fri 6/26/15	Thu 7/16/15															
14	Stage 2C/2D	30 days	Thu 6/4/15	Wed 7/15/15															
15	Pavement Removal	3 days	Thu 6/4/15	Mon 6/8/15															
16	Grading	6 days	Tue 6/9/15	Tue 6/9/15															
17	Paving	9 days	Wed 6/17/15	Mon 6/29/15															
18	ESC	3 days	Tue 6/30/15	Thu 7/23/15															
19	Signing	6 days	Fri 7/3/15	Fri 7/10/15															
20	Lighting	6 days	Wed 7/8/15	Wed 7/15/15															
21	Stage 3	35 days	Thu 7/16/15	Wed 8/26/15															
22	Stage 3A/3B	6 days	Thu 7/16/15	Thu 7/23/15															
23	Pavement Removal	2 days	Thu 7/16/15	Mon 7/20/15															
24	Grading	1 day	Fri 7/17/15	Mon 7/20/15															
25	Paving	2 days	Tue 7/21/15	Wed 7/22/15															
26	ESC	1 day	Thu 7/23/15	Thu 7/23/15															
27	Stage 3C	35 days	Thu 7/16/15	Wed 8/26/15															
28	Pavement Removal	5 days	Thu 7/16/15	Wed 7/22/15															
29	Grading	15 days	Thu 7/23/15	Wed 8/12/15															
30	Paving	10 days	Thu 8/13/15	Wed 8/26/15															
31	ESC	5 days	Thu 8/27/15	Wed 9/2/15															
32	Stage 3D	5 days	Thu 8/27/15	Wed 9/2/15															
33	Pavement Removal	1 day	Thu 8/27/15	Wed 9/2/15															
34	Grading	1 day	Fri 8/28/15	Fri 8/28/15															
35	Paving	2 days	Mon 8/31/15	Tue 9/1/15															
36	ESC	1 day	Wed 9/2/15	Wed 9/2/15															
37	Stage 4	35 days	Thu 9/3/15	Wed 10/21/15															
38	Stage 4A	16 days	Thu 9/3/15	Thu 9/24/15															
39	Grading	5 days	Thu 9/3/15	Wed 9/9/15															
40	Curb & Gutter	5 days	Thu 9/3/15	Mon 9/14/15															
41	Pav Scarification	1 day	Tue 9/15/15	Tue 9/15/15															
42	Paving	2 days	Wed 9/16/15	Thu 9/17/15															
43	ESC	5 days	Fri 9/18/15	Thu 9/24/15															
44	Stage 4B	3 days	Fri 9/25/15	Tue 9/29/15															
45	Pav Scarification	1 day	Fri 9/25/15	Fri 9/25/15															
46	Paving	2 days	Mon 9/28/15	Tue 9/29/15															
47	Stage 4C	16 days	Wed 9/30/15	Wed 10/21/15															
48	Grading	5 days	Wed 9/30/15	Tue 10/6/15															
49	Curb & Gutter	5 days	Mon 10/5/15	Fri 10/9/15															
50	Pav Scarification	1 day	Mon 10/12/15	Mon 10/12/15															
51	Paving	2 days	Tue 10/13/15	Wed 10/14/15															
52	ESC	5 days	Thu 10/15/15	Wed 10/21/15															

Project: Warren (51)
Date: Fri 1/30/15

CJ Moyna & Sons, Inc.
